

29/062026

Dear Resident / Business / Neighbour to the Lawnswood Roundabout,

Lawnswood Roundabout Scheme – Update

Welcome to our latest weekly update for the Lawnswood Roundabout scheme.


In area 9C (outside Weetwood Hall) the road crossing points are being installed so that power can be installed safely. Sewer connection works will be soon in this area. See below image taken earlier this month of this area.



In phase 4 (outside Lawnswood School) we are progressing with footpath works, including installing a dished drainage channel behind the kerbing. Signal pole installation is ongoing in this area. Aerial picture below.



In Phase 7 (by the Police station / sub-station) we are working north towards the station exit, preparing for kerb installations. Progress picture below taken earlier this month.

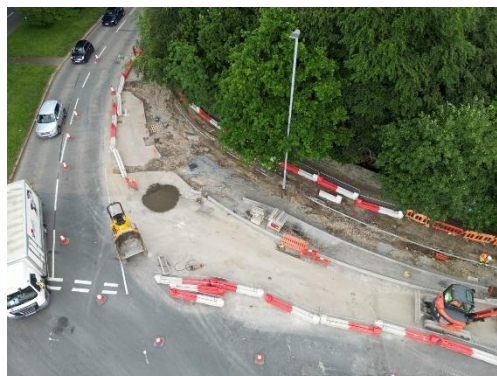

In phase 6 we are starting to install kerbs and traffic signal poles.

Eric Wright Civil Engineering Ltd
Sceptre House, Sceptre Way, Bamber Bridge, Preston, PR5 6AW
Tel: 01772 698822 www.ericwright.co.uk

Registered in England No. 256379

Please see overleaf for an indication of the phasing areas.

Upcoming night works – advance notice

During August and into early September there will be substantial carriageway works, firstly to prepare the subsurface of the new roadways, which will take place in sections around the roundabout, on all 4 approaches. These will be sequenced works and will involve diversions whilst the closures are in place. We are now required to do these night works from Mondays – Fridays so that there is no disruption to Leeds events, including the Iron Man and Leeds Festival weekends. The final surfacing works are scheduled for early September and will require full overnight closures of the roundabout and all approaches.

At present we are working with our subcontractors to align a programme which minimises disruption where possible, and the traffic management team to finalise diversion routes. We will then issue further updates about these works, together with diversion route plans.

We fully recognise that these works will be disruptive to local communities and we will ensure that information is circulated as soon as possible. The works are essential and have to be delivered in a certain way to ensure correct surfacing and longevity. Thank you in advance of your patience and understanding.

Feedback

As ever, we continue to welcome feedback which allows us to work closely with you during the project. You can contact us at any time at LawnswoodEnquiries@ericwright.co.uk

Thank you to everyone who continues to take care around the roundabout while works are in progress.

Further information about the scheme can be found here:

<https://lawnswoodroundabout.commonplace.is/>

Best wishes,

Lesley Davison

Public Liaison Officer

www.ericwright.co.uk/divisions/civil-engineering

Lawnswood Roundabout Phasing

